

PUNCH ITEM / P-024 / V1

Raise garage GFCI rough-in before wall close-in

Cooper Residence Renovation / CR-2026-017 / Residence / Garage / East wall / Entry door

RESPONSIBLE TRADE	PUNCH MANAGER	FINAL APPROVER	DUE DATE
Delta Electrical	Jordan Cho / Project Manager	Jordan Cho / Project Manager	2026-07-14

Deficiency

GFCI box centerline measures 12 inches above finished floor at the garage east wall.

Contract requirement

E1.1 Electrical Note 3 requires garage receptacle centerline at a minimum 18 inches AFF.

Required correction

Relocate the box so its centerline is at least 18 inches AFF before gypsum board installation.

Completion proof

Provide a completion photo showing the full wall context and a readable tape measurement from finished floor to box centerline.

Activity and chronology


TIME	ACTOR	EVENT
2026-07-12 10:18 PDT	Mike Alvarez	Field observation and three evidence assets captured.
2026-07-12 10:24 PDT	BUILI	E1.1 Rev 03 requirement linked; evidence package marked sufficient.

Evidence register


TYPE	EVIDENCE	LOCATION / CAPTURE
PHOTO	Garage east wall context Open stud wall near the garage entry door; GFCI rough-in visible.	Residence / Garage / East wall / Entry door 2026-07-12T10:18:00-07:00

TYPE	EVIDENCE	LOCATION / CAPTURE
MEASUREMENT	GFCI centerline tape measurement Tape shows receptacle centerline at approximately 12 inches AFF.	Residence / Garage / East wall / Entry door 2026-07-12T10:18:20-07:00
PHOTO	Receptacle rough-in detail Close view of the installed box before wall close-in.	Residence / Garage / East wall / Entry door 2026-07-12T10:18:38-07:00

Field image review

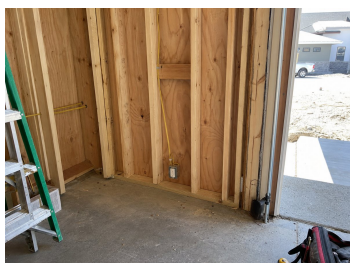

Garage east wall context

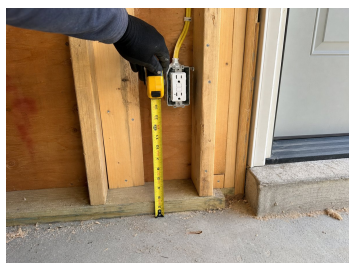

GFCI centerline tape measurement



Receptacle rough-in detail

Source index

Every requirement statement in this package must be checked against the exact document revision below. Superseded or unapproved sources cannot authorize work.

#	DOCUMENT / REVISION	PAGE	CITED REQUIREMENT
1	E1.1 / Rev 03 / APPROVED SHA-256: 85dceb1e6df4016fed87d520f d9c22a6049e351927123c6b587d69731 0a77fda	1	Electrical Note 3: Garage receptacle centerline shall be minimum 18 inches above finished floor.

Review control

REPORT ID	VERSION	GENERATED	CONTROL
rpt_demo_p024	1	2026-07-12 17:25 UTC	DRAFT / REVIEW REQUIRED

BUILI assembles a traceable review record. It does not make a design decision, authorize a change, determine contractual entitlement, or replace review by the responsible architect, engineer, contractor, or authority having jurisdiction.
